SURAT CITY POLICE · TRAFFIC BRANCH

Surat Police Traffic Report

September 2026

Monthly report · Previous Month (01 Sep 2026 – 30 Sep 2026)

Report ID
STR-20261010-0001

Generated
10 Oct 2026 14:19 IST

TOTAL VIOLATIONS	MOST COMMON VIOLATION	HIGHEST VIOLATION JUNCTION
431	**BRTS intrusion**	**Sahara Darwaja Junction**
+47.6% vs previous	189 cases (44%)	42 cases

AVERAGE QUEUE	AVERAGE SPEED	DATA COVERAGE
40.3 m	**30.4 km/h**	**100%**
Peak 78.0 m at Adajan Gam / Pat	3 of 22 junctions with adequate data	19 of 22 junctions below 50%

1 Executive summary

Report for Previous Month (01 Sep 2026 – 30 Sep 2026). A total of 431 traffic violations were recorded across the monitored network representing an increase of 47.6% compared to the previous period.


2 Key findings


Primary Infraction Modality
BRTS intrusion accounted for 189 cases (44% of total recorded violations).

Top Enforcement Hotspot
Sahara Darwaja Junction logged the highest number of violations (42 incidents).

Peak Congestion Corridor
Ring Road / Delhi Gate recorded the longest average queue at 40.8 m (peak 77.8 m).

3 Violations and trends

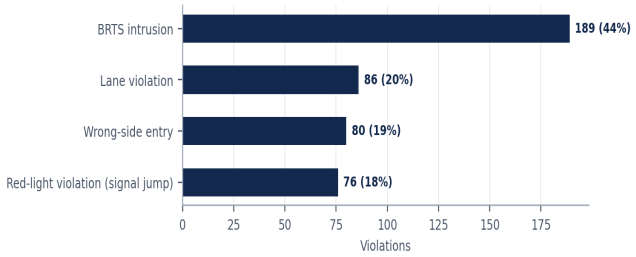

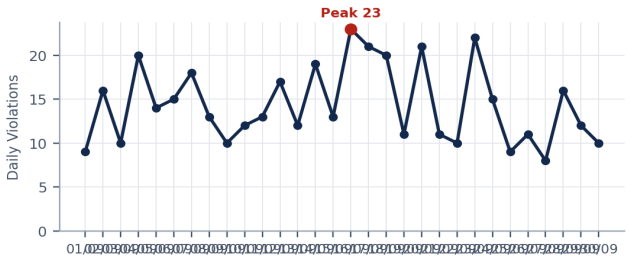

Primary Violation Hotspots

Rank	Junction Corridor	Infractions	Share of Total
1	Sahara Darwaja Junction	42	9.7%
2	Majura Gate Intersection	34	7.9%
3	Athwa Gate Junction	25	5.8%
4=	Udhna Darwaja	24	5.6%
4=	Cable Bridge Adajan Side	24	5.6%
6	Sarthana Jakatnaka	22	5.1%

4 Junction performance

Junction Corridor	Avg Queue	Peak Queue	Avg Speed	Congestion	Coverage
Ring Road / Delhi Gate	40.8 m	77.8 m	30.8 km/h	SEVERE	48% *
Adajan Gam / Patia	40.4 m	78.0 m	30.9 km/h	SEVERE	48% *
Khatodara GIDC Cross	40.4 m	77.9 m	30.3 km/h	SEVERE	48% *
Athwa Gate Junction	40.3 m	77.9 m	30.4 km/h	SEVERE	96%
Dindoli Bridge Approach	40.3 m	78.0 m	30.4 km/h	SEVERE	48% *
Sahara Darwaja Junction	40.3 m	77.7 m	30.6 km/h	SEVERE	96%
Majura Gate Intersection	40.2 m	77.9 m	30.3 km/h	SEVERE	96%
Katargam Darwaja	40.1 m	78.0 m	30.4 km/h	SEVERE	48% *
Vesu VIP Road Crossing	40.1 m	77.8 m	30.7 km/h	SEVERE	48% *
Udhna Darwaja	40.0 m	78.0 m	30.4 km/h	SEVERE	48% *
Piplod Junction	39.8 m	77.9 m	30.5 km/h	MODERATE	48% *
Varachha / Sardar Chowk	39.5 m	77.7 m	30.4 km/h	MODERATE	48% *
Kamrej Highway Junction	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Textile Market Corridor	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Palanpur Jakatnaka	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Sarthana Jakatnaka	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Cable Bridge Adajan Side	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Gopipura Main Road	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Bhatar Char Rasta	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Althan Canal Road	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Ichhapore GIDC Cross	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Dumas Beach Approach	0.0 m	0.0 m	0.0 km/h	LOW	0% *

Congestion level thresholds: Severe: 40 m and above · Moderate: 20 m to under 40 m · Low: under 20 m. Asterisk (*) denotes junctions with under 50% telemetry coverage.

5 Advisories and recommended actions

#	Priority	Target Location	Operational Advisory & Action Plan	Status
1	CRITICAL	Majura Gate Intersection	Deploy automated ANPR enforcement barricade and assign traffic warden. Observed when alert raised: Majura Gate Intersection: 78 m	Pending
2	CRITICAL	Varachha / Sardar Chowk	Issue automated challans via Surat Smart City camera integration. Observed when alert raised: Varachha / Sardar Chowk: 78 m	Pending
3	HIGH	Textile Market Corridor	Enforce strict no-stopping zone between 17:00 and 21:00.	Pending
4	HIGH	Ring Road / Delhi Gate	Enable dynamic queue flush phase on Eastbound approach. Observed when alert raised: Ring Road / Delhi Gate: 78 m	Applied

#	Priority	Target Location	Operational Advisory & Action Plan	Status
5	HIGH	Sahara Darwaja Junction	Increase North-South split by +14 seconds in Phase 2 adaptive cycle. Observed when alert raised: Sahara Darwaja Junction: 78 m	Applied
6	HIGH	Cable Bridge Adajan Side	Coordinate with Adajan Gam signal to throttle incoming flow.	Pending
7	MEDIUM	Udhna Darwaja	Extend dedicated BRTS green priority signal by 8 seconds. Observed when alert raised: Udhna Darwaja: 78 m	Pending
8	MEDIUM	Adajan Gam / Patia	Implement dynamic cycle length extension up to 135s. Observed when alert raised: Adajan Gam / Patia: 78 m	Applied

6 Data quality and method

• **Data Coverage:** 100.0% of expected telemetry samples were received across monitored network nodes. 19 junctions operated with under 50% coverage (Ring Road / Delhi Gate, Adajan Gam / Patia, Khatodara GIDC Cross, Dindoli Bridge Approach).
• **Definitions:** Network averages reflect reporting junctions weighted by sample count. Congestion levels follow approach queue depth. All timestamps and daily buckets are in Indian Standard Time (IST).
• **Analytical Methodology:** Narrative generated deterministically via local statistical template. All figures derived from municipal database registers.
• **Limitations:** Figures reflect system-detected and confirmed events. Peak queue values of 78 m recorded at several junctions may be capped by the sensor measurement range. Signal timing modifications should be coordinated with the Traffic Police Command Center.

Report ID: STR-20261010-0001 | **Data Fingerprint:** FC9D-69F4-D467-075C | **Source:** Municipal Traffic Register

Prepared by	Reviewed by	Approved by
Name / Designation Date	Name / Designation Date	Name / Designation Date
