SURAT CITY POLICE · TRAFFIC BRANCH

Surat Police Traffic Report

28 Sep to 04 Oct 2026

Weekly report · Previous Week (28 Sep 2026 – 04 Oct 2026)

Report ID
STR-20261010-0001

Generated
10 Oct 2026 14:19 IST

TOTAL VIOLATIONS	MOST COMMON VIOLATION	HIGHEST VIOLATION JUNCTION
88	**BRTS intrusion**	**Majura Gate Intersection**
+2.3% vs previous	32 cases (36%)	6 cases (joint highest)
AVERAGE QUEUE	**AVERAGE SPEED**	**DATA COVERAGE**
40.0 m	**30.5 km/h**	**34%**
Peak 77.9 m at Athwa Gate Junct	12 of 22 junctions with adequate data	22 of 22 junctions below 50%

1 Executive summary

Report for Previous Week (28 Sep 2026 – 04 Oct 2026). A total of 88 traffic violations were recorded across the monitored network representing an increase of 2.3% compared to the previous period. Telemetry sensor coverage was 33.6%; queue and velocity indicators reflect reporting junctions.


2 Key findings


Primary Infraction Modality
BRTS intrusion accounted for 32 cases (36% of total recorded violations).

Top Enforcement Hotspots
Majura Gate Intersection, Ichhapore GIDC Cross tied for the highest violation count with 6 incidents each.

Peak Congestion Corridor
Athwa Gate Junction recorded the longest average queue at 41.5 m (peak 77.9 m).

3 Violations and trends

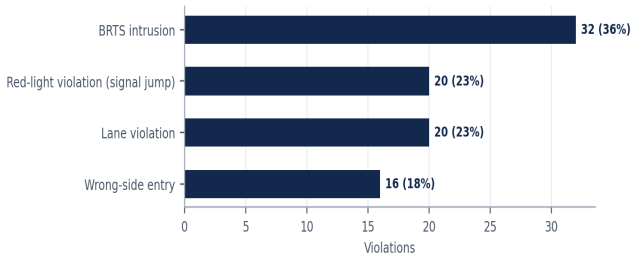

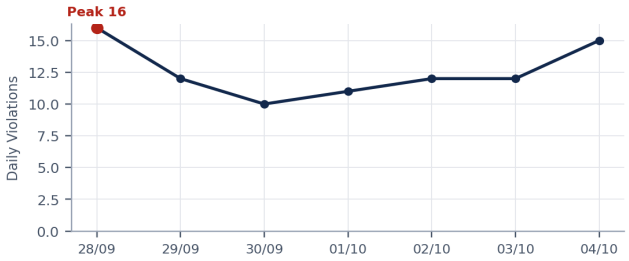

Primary Violation Hotspots

Rank	Junction Corridor	Infractions	Share of Total
1=	Majura Gate Intersection	6	6.8%
1=	Ichhapore GIDC Cross	6	6.8%
1=	Althan Canal Road	6	6.8%
4=	Sahara Darwaja Junction	5	5.7%
4=	Ring Road / Delhi Gate	5	5.7%
4=	Katargam Darwaja	5	5.7%

4 Junction performance

Junction Corridor	Avg Queue	Peak Queue	Avg Speed	Congestion	Coverage
Athwa Gate Junction	41.5 m	77.9 m	30.7 km/h	SEVERE	22% *
Piplod Junction	41.5 m	77.9 m	30.5 km/h	SEVERE	15% *
Katargam Darwaja	41.0 m	77.9 m	30.7 km/h	SEVERE	15% *
Adajan Gam / Patia	40.4 m	76.3 m	30.1 km/h	SEVERE	15% *
Dindoli Bridge Approach	40.2 m	76.3 m	29.9 km/h	SEVERE	15% *
Majura Gate Intersection	40.2 m	77.9 m	30.8 km/h	SEVERE	22% *
Sahara Darwaja Junction	39.8 m	77.5 m	30.3 km/h	MODERATE	22% *
Khatodara GIDC Cross	39.3 m	77.7 m	30.5 km/h	MODERATE	15% *
Vesu VIP Road Crossing	39.3 m	76.5 m	30.7 km/h	MODERATE	15% *
Ring Road / Delhi Gate	39.0 m	75.8 m	30.9 km/h	MODERATE	15% *
Varachha / Sardar Chowk	38.8 m	77.7 m	30.3 km/h	MODERATE	15% *
Udhna Darwaja	38.0 m	76.0 m	30.7 km/h	MODERATE	15% *
Kamrej Highway Junction	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Textile Market Corridor	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Palanpur Jakatnaka	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Sarthana Jakatnaka	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Cable Bridge Adajan Side	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Gopipura Main Road	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Bhatar Char Rasta	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Althan Canal Road	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Ichhapore GIDC Cross	0.0 m	0.0 m	0.0 km/h	LOW	0% *
Dumas Beach Approach	0.0 m	0.0 m	0.0 km/h	LOW	0% *

Congestion level thresholds: Severe: 40 m and above · Moderate: 20 m to under 40 m · Low: under 20 m. Asterisk (*) denotes junctions with under 50% telemetry coverage.

5 Advisories and recommended actions

#	Priority	Target Location	Operational Advisory & Action Plan	Status
1	HIGH	Textile Market Corridor	Enforce strict no-stopping zone between 17:00 and 21:00.	Pending
2	MEDIUM	Athwa Gate Junction	Coordinate green wave offset with Majura Gate intersection (+18s lead). Observed when alert raised: Athwa Gate Junction: 78 m	Pending
3	MEDIUM	Udhna Darwaja	Extend dedicated BRTS green priority signal by 8 seconds. Observed when alert raised: Udhna Darwaja: 76 m	Pending
4	LOW	Piplod Junction	Deploy automated weekend timing plan with +12s green on Dumas approach. Observed when alert raised: Piplod Junction: 78 m	Pending

6 Data quality and method

• **Data Coverage:** 33.6% of expected telemetry samples were received across monitored network nodes. 22 junctions operated with under 50% coverage (Athwa Gate Junction, Piplod Junction, Katargam Darwaja, Adajan Gam / Patia).
• **Definitions:** Network averages reflect reporting junctions weighted by sample count. Congestion levels follow approach queue depth. All timestamps and daily buckets are in Indian Standard Time (IST).
• **Analytical Methodology:** Narrative generated deterministically via local statistical template. All figures derived from municipal database registers.
• **Limitations:** Figures reflect system-detected and confirmed events. Peak queue values of 78 m recorded at several junctions may be capped by the sensor measurement range. Signal timing modifications should be coordinated with the Traffic Police Command Center.

Report ID: STR-20261010-0001 | **Data Fingerprint:** B4FE-B93E-F390-F640 | **Source:** Municipal Traffic Register

Prepared by	Reviewed by	Approved by
Name / Designation Date	Name / Designation Date	Name / Designation Date
